



# MINE ACTION PROGRAMME OF AFGHANISTAN

## ANNUAL OPERATIONAL WORK PLAN

1398 - (April 19 to March 2020)  
Second version (July 2019)

WORKING TO MAKE AFGHANISTAN MINE-FREE BY MARCH 2023



## Table of Contents

Acronyms .....	ii
Introduction .....	1
The Mine Action Programme of Afghanistan .....	1
Background of the Operational Work Plan .....	1
DMAC Priority Areas for 1398: .....	1
Chapter One: Overview .....	3
1.1 Background .....	3
1.1.1 Remaining Mine and ERW Contamination .....	3
1.1.2 Explosive Remnants of War Contamination .....	3
1.1.3 Civilian Casualties .....	4
1.2 Afghanistan Mine Ban Convention Extension Plan .....	4
1.2.1 1398 Funding .....	6
1.3 The Convention on Cluster Munitions (CCM) .....	6
1.4 The Convention on Certain Conventional Weapons (CCW) .....	6
1.5 The Convention on the Rights of Persons with Disabilities (CRPD) .....	7
Chapter Two: Activities .....	7
2.1 Programme Management and Advocacy .....	7
2.1.1: Advocacy, Planning and Communications .....	7
2.1.2 Research and Development .....	12
2.1.3 Quality Assurance and Quality Control .....	15
2.1.4 Information Management .....	15
2.2 Survey and Clearance .....	17
2.2.1 Survey .....	17
2.2.2 Clearance (explosive hazard reduction) .....	19
2.3 Victim Assistance .....	25
2.4 Mine and Explosive Remnants of War Risk Education .....	29
2.5 Gender & Diversity Mainstreaming: .....	31
Chapter Three: Roles and Responsibilities .....	33
Chapter Four: Risk Management .....	34
Annex A. 1398 Demining Projects, targeted and planned as of July 2019 .....	36
Annex B. List of NTS Planned Districts for 1398 .....	41

## Acronyms

AAR	Association for Aid and Relief
ACBL	Afghan Campaign to Ban Landmines
AGE	Anti-Government Elements
AIM	Abandoned Improvised Mine
ANDMA	Afghanistan National Disaster Management Authority
AMAS	Afghanistan Mine Action Standards
ANSF	Afghan National Security Forces
APMBC	Anti-Personnel Mine Ban Convention
ATC	Afghan Technical Consultants
AV mines	Anti-Vehicle mines
AP mines	Anti-Personnel mines
CCW	Convention on Certain Conventional Weapons
CRPD	Convention on the Rights of Persons with Disabilities
CSSF	Conflict Stability Security Fund
DAFA	Demining Agency for Afghanistan
DDG	Danish Demining Group
DFID	United Kingdom Department for International Development
DMAC	Directorate of Mine Action Coordination
ERW	Explosive Remnants of War
GAGP	Grant Assistance for Grassroot Projects
GFFO	German Federal Foreign Office
GIS	Geographical Information System
HALO Trust	Hazardous Area Life Support Organisation Trust
IDP	Internally Displaced Person
IM	Improvised Mine
IMSMA	Information Management System for Mine Action
IP	Implementing partners
MAPA	Mine Action Programme of Afghanistan
MBC	Mine Ban Convention
MCPA	Mine Clearance and Planning Agency
MDC	Mine Detection Centre
MEIFCS	Mine/ERW Impact Free Community Survey
M/ERW RE	Mine and Explosive Remnants of War Risk Education
MIS	Management Information System
MoD	Ministry of Défense
MoE	Ministry of Education
MoI	Ministry of Interior
MMD	State Ministry for Martyrs and Disability
MoPH	Ministry of Public Health
NATO	North Atlantic Treaty Organisation
NGO	Non-Governmental Organisation
NOFO	Notice of Funding Opportunity
NPA	Norwegian People's Aid

NTS	Non-Technical Survey
OMAR	Organisation for Mine Clearance and Afghan Rehabilitation
PDIA	Post Demining Impact Assessment
PwD	Person with Disabilities
QA	Quality Assurance
QC	Quality Control
QM	Quality Management
R&D	Research and Development
RNG	Royal Netherlands Government
SOP	Standing operating procedure
TOT	Training of Trainers
UNMAS	United Nations Mine Action Service
VA	Victim Assistance
VTF	Voluntary Trust Fund
WAD	Weapons and Ammunition Destruction team

## Introduction

### The Mine Action Programme of Afghanistan

The Mine Action Programme of Afghanistan (MAPA), one of the world's largest and longest-established mine action programmes, is managed by the Directorate of Mine Action Coordination (DMAC) under the authority of Afghanistan National Disaster Management Authority (ANDMA) which is headed by the State Minister for Disaster Management and Humanitarian Affairs. DMAC works in close partnership with national and international organizations that provide a range of services designed to minimize the impact of mines and explosive remnants of war (ERW).

There are currently 47 accredited mine action organizations which are eligible to conduct mine action activities in 1398<sup>1</sup>; 16 national non-government organizations (NGOs), nine international NGOs, 18 national commercial companies, and four international commercial companies. The list of accredited mine action NGOs and commercial companies is available at [www.dmac.gov.af](http://www.dmac.gov.af).

### Background of the Operational Work Plan

The MAPA 1398 Operational Work Plan reflects the policies and planning procedures put in place by the DMAC and is in line with the National Mine Action Strategic Plan 2016-2020. The workplan is a point of reference for the design, implementation, monitoring and evaluation of all mine action interventions in Afghanistan. This document contains data analysis describing the nature and scope of mine action-related challenges in Afghanistan, the intended activities for 1398 with confirmed and committed funding, and the prioritization and quality management regime set out by the DMAC. The data presented in this document is valid as of 1 July 2019; a detailed data analysis is available at [www.dmac.gov.af](http://www.dmac.gov.af).

### DMAC Priority Areas for 1398:

DMAC and the IPs priority areas for 1398 are as follows:

- Reduce civilian casualties
- Build the capacity of mine action to respond to the emerging problem of abandoned improvised mine (AIM)
- Improve the quality management system
- Establish a sustainable civilian data collection
- Conduct a national survey to identify the scope of new contamination
- Establish a standalone research and development cell
- Establish deminers database to collect all records of deminers trained by all IPs
- Finalize liability policy for further use
- Search for new survey tools and its application in the programme
- Seek for proper utilization of Mine Detection Dogs (MDD)
- Functionalize the centre of excellence

The MAPA should achieve the following during 1398:

---

<sup>1</sup>1398 of the Solar Islamic Calendar is equivalent to 21 March 2019 – 20 March 2020 of the Gregorian Calendar.

- Conduct non-technical survey (NTS) of 29 districts in 6 regions, including NTS of recent contamination. Details on [page 17](#).
- Release 75.6 sq. km of known legacy-contaminated land<sup>2</sup>. Details are available on [page 18](#).
- Provide Mine/ERW risk education to 781 impacted communities and at UNHCR encashment centres. Details are available on [page 27](#).
- Survey 600 villages for the possible presence of ammunition bunkers by Weapons and Ammunition Disposal (WAD) teams. Details can be found on [page 24](#).
- Conduct around 2,200 external quality assurance (QA) monitoring and quality control (QC) visits to mine action projects and teams. Details can be found on [page 13](#).
- Conduct post-demining impact assessments (PDIA) of 85 closed contaminated areas, and livelihood surveys in 12 communities of Kapisa province. Details on [page 30](#).

---

<sup>2</sup> Legacy contamination is contamination left from previous conflicts which occurred before 2001.

# Chapter One: Overview

## 1.1 Background

### 1.1.1 Remaining Mine and ERW Contamination

As of end of June 2019, data suggests that there are 3,841 hazardous areas covering 1,756.4 sq. km of land in Afghanistan. This consists of 619.1 sq. km of legacy contamination<sup>3</sup> and 1,137.3 sq. km of new contamination<sup>4</sup> made up of improvised mines (IMs) and Explosive Remnants of War (ERW).

### 1.1.2 Explosive Remnants of War Contamination

Clashes between Anti-Government Elements (AGEs), NATO<sup>5</sup> and the Afghan National Security Forces (ANSF) since 2001 has posed a major challenge, as most of these incidents have left behind unexploded ordnance and/or AIMs. Through the High Explosive Training Ranges forum, chaired by NATO Resolute Support, the programme is in contact with relevant military authorities from NATO to receive information on the location of each armed conflict incident that has occurred so far. Thus, these sites can be surveyed and the scope of ERW contamination post-2001 can be determined. Cross-border shelling from Pakistan in eastern provinces such as Kunar is another cause of contamination that leaves ERW behind.

During 1396, a comprehensive concept note was prepared and submitted to the Office of the President of the Islamic Republic of Afghanistan for the survey and clearance of 219 newly contaminated areas covering approximately 416<sup>6</sup> sq. km of land in 14 provinces contaminated with ERW and improvised mines (IM).

During 1398 DMAC, through Quick Response Teams (QRTs), will contribute in the NTS of the ERW sites for further confirmation and availability of these hazards.

Moreover, it is worth-mentioning, ERWs and IMs are also having impact on returnees and deportees. there are currently 2.4 million Afghan refugees residing in Pakistan facing repatriation to Afghanistan who are unaware of the ERW risks and where ERW contamination exists.

### *Abandoned Improvised Mine (AIM) Clearance Operations:*

The overwhelming challenge of AIM contamination and the number of civilian casualties from this contamination call for additional measures to address this challenge. The term AIM refers to Victim Operated Improvised Explosive Devices (VOIED). The prefix of abandoned is used to define the fact that the humanitarian demining organizations only deal with those victims operated IEDs that remain in areas where conflict has taken place and after the cessation of armed conflicts the presence of these devices pose a threat to the lives and livelihoods of civilians. Humanitarian demining organizations, in order to maintain its neutral nature, do not deal with other types of IEDs such as remote control, body-borne, vehicle-borne etc. In case of receiving such requests for clearance of other than the VOIEDs, DMAC and MAPA organizations refers them to the ministry of interior.

To be prepared for effective and efficient survey and clearance operations as well as QA and QC of abandoned improvised mine operations, DMAC is intended to coordinate finding possible ways for building the capacity of demining organizations as well as its QM staff. Building this capacity within the MAPA will ensure safe and efficient operations for survey and clearance of improvised mine contaminated areas in Afghanistan. DMAC has already drafted the AMAS chapter for AIM clearance operations and it is expected that the demining organizations develop their Standing Operating Procedures (SOPs) in light of the AIM clearance standards. In

<sup>3</sup> This includes 480.5 sq. km of MF, 85.2 sq. km of BF and 53.4 sq. km of IHA hazards

<sup>4</sup> This includes 60.3 sq. km BF, 33.7 sq. km AIM, 412.2 sq. km IHA and 630.9 sq. km Firing Range area.

<sup>5</sup> NATO was involved in fighting until 2014 and then changed its role to supporting and training ANSF.

<sup>6</sup> Initially this figure was 421.7 sq. km, during the last year 3.8 sq. km area has been cancelled while the remaining 417.9 sq. km remain for NTS

general, the capacity of demining organizations which are going to be engaged in survey and clearance of AIM should be built on the following:

- The concept of operations of humanitarian IM clearance
- Carry out a comprehensive assessment of the threat, based on local non-state armed group capability, intent and operating environment
- Conduct NTS of AIM contaminated areas
- Identifying the components used in the construction of IMs, whilst carrying out humanitarian IM clearance operations
- The actions to be carried out in the event of discovering of IMs during humanitarian mine action clearance operations
- Render safe procedure (RSP) and demolition of improvised mines
- Conduct QA and QC of IM survey and clearance operations

During 1398, DMAC will try to identify and coordinate possible sources of training to develop and build the capacity within the MAPA for conducting survey and clearance operations of AIM contaminated areas as well as conducting QA and QC of such operations. DMAC will also provide technical support to demining organizations for developing their relevant SOPs.

### 1.1.3 Civilian Casualties

According to the DMAC's Information Management System for Mine Action (IMSMA), during 2018 the average number of civilian casualties recorded was 118 per month, which demonstrates an approximately three-fold increase compared to 2013.

According to UNAMA's Protection of Civilians Annual Report, 2018<sup>7</sup> the civilian casualties from victim-activated pressure-plate IEDs decreased by 26 per cent in 2018, causing 753 civilian casualties (269 deaths and 484 injured). UNAMA also recorded an eight per cent decrease in civilian casualties from remote-controlled IEDs that caused 505 civilian casualties (96 killed and 409 injured), and a 91 per cent increase in magnetic IEDs that caused 262 civilian casualties (34 deaths and 228 injured).

Between 1 January and 31 December 2018, UNAMA documented 492 civilian casualties (150 deaths and 342 injured) due to explosive remnants of war, a 23 per cent decrease compared to 2017. In line with the trend observed in 2017, this decrease may be attributed to factors such as the clearance of ERW from the battlefield, together with ongoing education programmes. Children continued to be disproportionately harmed by ERW. In 2018, they accounted for 87 per cent of all civilian casualties from explosive remnants of war, with 426 child casualties (136 deaths and 290 injured) recorded by UNAMA including 367 boys. Children who survive encounters with ERW live with a lasting detrimental impact on their quality of life due to loss of limbs or eye-sight, other serious injuries, and psychological trauma.

## 1.2 Afghanistan Mine Ban Convention Extension Plan

The Government of the Islamic Republic of Afghanistan (GoIRA) submitted a clearance extension request at the Anti-Personnel Mine Ban Convention meeting in April 2012. By submitting this


---

<sup>7</sup> United Nations Assistance Mission to Afghanistan. (2018). Protection of Civilians Annual Report, 2018. Kabul: UNAMA. Retrieved from [https://unama.unmissions.org/sites/default/files/afghanistan\\_protection\\_of\\_civilians\\_annual\\_report\\_2018\\_final\\_Feb\\_2019.pdf](https://unama.unmissions.org/sites/default/files/afghanistan_protection_of_civilians_annual_report_2018_final_Feb_2019.pdf)



extension request Afghanistan committed to clearing all known mine contaminated areas in its territory by March 2023. The below graph shows the original baseline target indicated in the extension plan, the revised target of clearance which is updated yearly, and the amount of cleared areas as of July 2019.


*Graph 1: Annual area baseline target, updated target and processed area.*



As shown in the above graph, there are 683sq. km of remaining contamination to be cleared by the Afghan year 1401 (March-2023). Moreover, there is an extra 412 sq. km of new contamination to be surveyed and cleared which has not been added to this graph as it requires a comprehensive non-technical survey (NTS) to establish accurate figures and details on the extent and type of contamination; subsequently, it will be added to the target for the remaining years.

The graph below shows the funding requirements of the original extension plan, the revised funding target, the funding secured so far, and the funding needed for the remaining years to complete the extension plan on time as of July 2019.

*Graph 2: Annual funding initial target, updated target and secured funding.*

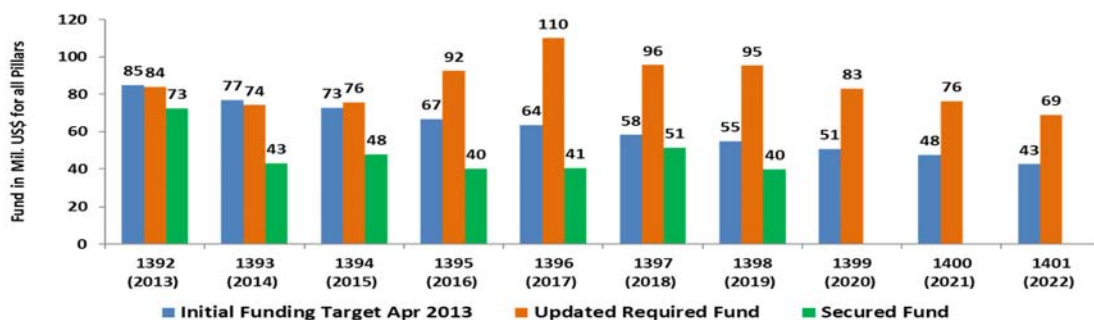


As displayed in the graph, the full amount of funding for the extension was not secured in the first six years; now in the seventh year of the plan, only 42 per cent of required funding is secured against the annual funding target until July 2019. Meanwhile, the legacy and new contaminations have been reported by Mine/ ERW Impact Free Community Surveys (MEIFCS) and NTS, and this, combined with the funding shortfalls from previous years, places an extra burden on the funding requirements for each subsequent year. Each year the plan is reviewed and the unfunded projects from previous years and newly reported contamination are taken into account. The MAPA is continuously considering innovative ideas to reduce the cost of clearance; however, despite these efforts, the extension plan will not be achieved if the current funding trend continues.

### 1.2.1 1398 Funding

The required funding for 1398 is \$95.3 million USD and as of July 2019, 42 per cent of this target has been secured. The graph below shows the required funding and funding secured for each mine action pillar.

*Graph 3: 1398 funding initial target, updated target, secured and outstanding in million US\$*

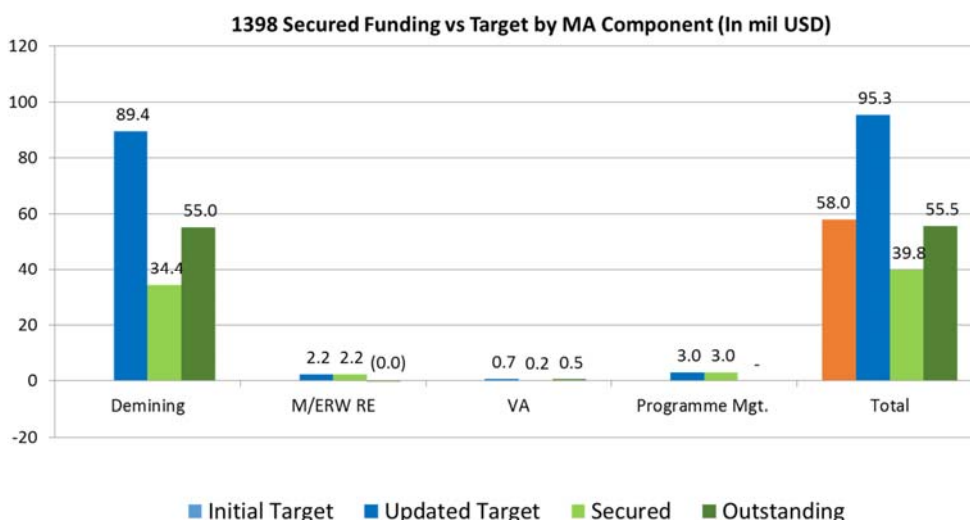

### 1.3 The Convention on Cluster Munitions (CCM)

The GoIRA signed the Convention on Cluster Munitions (CCM) on 3 December 2008, ratified it on 8 September 2011, and entered it into force on 1 March 2012.

There was 2,302 recorded hazards in which the device type was CM as standalone or CM with ERW, out of which 2,294 sites have been cleared covering 456.2 sq. km, while, 8 CM recorded hazards covering 5.8 sq. km area still exist from which 5 of them (3.3 sq. km) are part of confirmed fund by IPs to be cleared during this year and 3 CM hazards covering 2.56 sq. km area are with open status, would be planned in any upcoming funding opportunity.

### 1.4 The Convention on Certain Conventional Weapons (CCW)

On 9 August 2017, Afghanistan joined the Convention on Certain Conventional Weapons (CCW) with all of its five protocols, including, the Amended Protocol II on Mines, Booby-Traps and Other Devices; and Protocol V on Explosive Remnants of War (ERW). Afghanistan is the 125<sup>th</sup> state party to the CCW.

The ERW contamination from both legacy and new contamination causes over 40 per cent of current civilian casualties. There are 134 sq. km of legacy ERW contamination recorded and 187 sq. km of new ERW contamination. So far, new contamination is reported from 14 affected provinces out of 34 provinces of the country, though the problem could be much more extensive.

DMAC management is advocating to establish a mechanism to closely work with Ministry of Defence (MoD) and Ministry of Interior (MoI) in order to convince them for clearing the contaminated areas following their military operations.

## 1.5 The Convention on the Rights of Persons with Disabilities (CRPD)

The convention was adopted by the United Nations General Assembly on 13 December 2006 and opened for signature on 30 March 2007; it entered into force on 3 May 2008. The convention was ratified by the government of Afghanistan in 2011. DMAC provides technical assistance to State Ministry for Martyrs and Disability for the effective implementation of the CRPD. Currently MMD is part of the committee working on the first UNCRPD report

## Chapter Two: Activities

This section describes the activities that will be implemented during the course of 1398.

### 2.1 Programme Management and Advocacy

DMAC, with its seven regional offices, is the primary entity responsible for leading the programme management of mine action activities in Afghanistan, while the implementing partners and the UNMAS act as focal points in their areas of operations with UN agencies, communities, government authorities and other national and international development organisations.

#### 2.1.1: Advocacy, Planning and Communications

##### **Advocacy**

Advocacy plays a vital role in humanitarian mine action in order to build consensus and encourage cooperation among different mine action stakeholders and parties to the conflict to provide a safe environment for mine and ERW affected communities, promote the rights of persons with disabilities and mobilise resources for the programme. Some of the forums the MAPA will be using for advocacy in 1398 are listed in the below table.

*Table 1: Advocacy events*

Event	Purpose	Date	Progress Tracking
International Day of Mine Awareness and Assistance in Mine Action	To commemorate the efforts made in mine action by all stakeholders and acknowledge the path ahead toward Ottawa Treaty compliance and zero mine action casualties.	April 2019	Done
Afghanistan Donor & Implementing Partners Coordination Workshop for Mine Action	To discuss the achievements and challenges of the MAPA against the backdrop of increasing casualty numbers and development barriers.	26-28 March 2019	Done

Anti-Personnel Mine Ban Convention (APMBC) – Intersessional Meetings.	Mid-year assessment of the States parties to the APMBC and the key issues the States parties are seized with.	June 2019	Done
Conference of States Parties to the CRPD.	Advocacy for the rights of persons with disabilities and to highlight the key concerns for this group of persons in Afghanistan.	June 2019	Done
International Day of Peace	To commemorate the efforts made in mine action by all stakeholders and acknowledge the path ahead toward Ottawa Treaty compliance and zero mine action casualties.	September 2019	
Meeting of States Parties to the Convention on Cluster Munitions.	Meeting to discuss progress on the prohibition on use and stockpiling and clearance of cluster munitions.	September 2019	
Meeting of high contracting parties on Protocol V and the Convention on Certain Conventional Weapons (CCW).	Meeting to discuss Afghanistan’s progress and measures on the restriction on the use of certain conventional weapons which could be extremely injurious or have indiscriminate effects.	November 2019	
APMBC – Meeting of the States Parties	Advocacy and resource mobilization for funding to contribute to the prohibition of the use, stockpiling, production and transfer of anti-personnel mines. Afghanistan is currently presiding over the Ottawa Treaty and will hand over its Presidency of the Treaty to Norway, highlighting the achievements and focus it has made over the past 12 months nationally and globally.	November 2019	
Donor meetings	To mobilize resources for the programme	Ad/Hoc	

***The Afghan Campaign to Ban Landmines (ACBL)***

The Afghan Campaign to Ban Landmines (ACBL) was established on 5 August 1995 in Kabul as a non-governmental and non-political forum advocating for a total ban on landmines. From 1995 – 2010, ACBL successfully played its role in banning landmines.

In 2018, after a seven-year break, the ACBL re-started its work by conducting a workshop on electing the steering committee and then the chairperson of the steering committee by the elected steering committee members. Significant steps were taken during 2018 by developing Standard Working

Procedure (SWP) for ACBL steering committee, developing an action plan and organizing meetings with government National Security Forces and AGEs for support and implementation of APMBC, CCW and other relevant conventions.

The purpose of ACBL is to respond to:

- The new obstacles faced by the programme due to a deteriorating security situation and the increased risks faced by the operators in the field.
- The new contamination and expansion of hazardous areas due to an increase in the production and use of improvised mines and ERW.
- Funding shortfall to achieve a mine-free Afghanistan by 2023.
- The limitations in fulfilling the requirements of the Convention on the Rights of Persons with Disabilities (CRPD) for a full inclusion of mine/ERW victims in society.

The ACBL plans to do the following in 1398:

Action	Date	Progress Tracking
Mine Action Awareness day celebration by ACBL, Implementing Partners (IPs) and DMAC	4 April 2019	As DMAC celebrated, so ACBL Cancelled it.
Peace day celebration by ACBL, UNMAS and DMAC in each region	Sep 2019	
Conduct a national ACBL conference	4 <sup>th</sup> Quarter 2019	
Organise meetings with government National Security Forces and AGEs for support and implementation of APMBC, CCW and other relevant conventions	Throughout the year	
Disability day coordinated by ACBL with MMD and other stakeholders	3 Dec 2019	
Programs to engage the government, the security council, armed groups, particularly the Taliban, and the peace council. (ACBL with UNMAS)	Throughout the year	

### **Planning**

The MAPA’s workplan for 1398 is in line with the Mine Ban Convention (MBC) extension workplan, the National Mine Action Strategic Plan (2016-2020) and the DMAC portfolio submission to the MBC extension for 1398. As per the MBC workplan, to meet the end goal of making Afghanistan free of known mine/ERW contamination, the programme needs to clear 143 sq. km of land during 1398; as of March 2019, funding to clear around 45 sq. km has been obtained and the programme will continue its fundraising efforts in order to clear the remaining area.

The National Mine Action Strategic Plan (2016-2020) has four main goals which are: 1) Facilitating Development, 2) Engagement with other sectors, 3) The pillars of mine action (preventive and responsive), and 4) Gender & diversity mainstreaming. Under each goal, there are numerous objectives linked to several action plans. A committee is established within DMAC, with support from the main implementing partners (IPs), to execute the action plans.

A numerical summary of the four main goals, the relevant objectives and its activities are shown below with the progress made until July 2019.

*Table 2: MAPA strategic goals*

S- No	Goals	No. of Objectives	No. of Action Plans	Progress		Awaiting for Action
				No. of Completed Action Plans	No. of Ongoing Action Plans	
1	Facilitating Development	3	8	2	5	1
2	Engagement with other sectors	9	28	8	15	5
3-1	5 pillars of mine action - Preventive functions	8	24	1	20	3
3-2	5 pillars of mine action - Responsive functions	5	16	4	11	1
4	Gender & Diversity Mainstreaming	7	24	8	13	3
<b>Total</b>		<b>32</b>	<b>100</b>	<b>23</b>	<b>64</b>	<b>13</b>

### External Relations

The DMAC Advocacy and External Relations Department is responsible for raising awareness and communicating the main objectives and achievements of the MAPA. To meet its goals, the External Relations department is planning the following main activities during 1398.

*Table 3: List of external relations activities for 1398.*

Action	Objective	Result	Progress Tracking
MAPA External Relations department working group meetings every other month.	Develop a common strategy with activities and objectives.	Activities developed regarding the International Days during 1398 and/or International and National events.	Ongoing
Daily media monitoring.	Correct any misinformation or discrepancies with the information provided by any organization or individual.	Share updated information and correct any discrepancies if necessary.	Ongoing on daily bases
Develop and distribute relevant publications (Mine Action glossary, Woman in Mine Action and a Mine Action Acronyms Guide) to all MAPA stakeholders.	The documents will convey messages on MAPA's achievements, success stories, objectives and challenges.	Publication of these materials and mine action awareness for the social media. A hard copy of the newsletter should be sent to government offices and a soft copy sent via email.	Ongoing
Organize public activities to work closely with Afghan civil society. Some of the proposed activities are: workshops, radio programmes, mine awareness paint/music etc.	The aim of this project is to gain civil society support for mine action to better advocate for public, government and the international community's support for the programme.	An increase in engagement and awareness within civil society, the government and the international community.	Ongoing MRE Messages on the TV shows
Develop a video every six months.	A 1-5-minute video will be developed every six months for advocacy efforts.	The video will be posted on the different social media channels and played at events, workshops, etc.	We send s concept note to UNMAS and waiting for approval.

Action	Objective	Result	Progress Tracking
Organize a field visit once a month.	Every month External Relation staff will travel to the field to work with local counterparts, interview people and get photos for the External Relation department.	Material from the field will be used to create External Relations products, such as campaigns and advertising and will be used for publications.	For the first quarter of 1398 (April-June) due to lack of funds and other urgent prioritise no filed visits were contradicted.
Create a strong daily social media campaign for Facebook:  @DMAC. Afghanistan and Twitter: @Dmac.afg	During 1398, the digital communication channels (Facebook and Twitter) will have one daily post focused on advocacy and mine awareness. During special International Days, a special campaign will run at the same time.	Increase the likes and the visits (average 100 likes every month / paid online advertising for Facebook-Twitter accounts to get more likes)	Ongoing
Maintain and update the website.	Update the content and images of the website weekly. Make sure all the links work and the information can be accessed by everybody.	Website updated.	Ongoing
Develop the following External Relations products: Annual Report 1397; Infographic for 1397; MAPA Fast Facts (Quarterly); MAPA Newsletter (Quarterly); Post Deming Impact Assessment (PDIA) Report for 1398; Mine Action and Livelihood Survey Report 1398.	During 1398, the External Relations department will develop updated products with technical information about Mine Action in Afghanistan. These products will be published bimonthly, quarterly and annually.	Publication of these materials and mine action awareness from the media. A hard copy of the newsletter should be sent to government offices or a list of their email addresses need to be prepared.	Ongoing quarterly

### 2.1.2 Research and Development

Research and development (R&D) play a very important role in the effectiveness and efficiency of mine action operations. Therefore, DMAC plans to increase efforts to enhance the success of mine action operations during 1398. The R&D activities listed below will be conducted during 1398. They will be conducted using suitable approaches such as trials, quality circles, studies, field visits and consulting with the team of experts from demining organizations.



Table 4: List of Research and Development areas for 1398.

S. #	Activity	Time Frame	Responsible Department	Progress Tracking
1	To conduct an Operation Technical Workshop by participating DMAC HQ OPS staff, DMAC ROs, UNMAS OPS Staff and IPs OPS Managers.	Apr – May 2019	Operations	Completed
2	Develop a policy for better management and control of commercial demining operations.	Apr – June 2019	Operations	Completed & the policy officially released
3	Develop and sign an MoU with ANSF (MOI, MOD and NDS) regarding AIM clearance operations.	May-July 2019	Operations	The initial draft already shared with Mol & MoD
4	To conduct a case study on a mechanical excavator (rip and follow up) in order to find out its productivity, efficiency and its operation	Oct- 2019 Feb 2020	Operations in coordination with regional offices	
5	To establish MDU & Anti-Vehicle (AV) clearance TWG.	Apr-May 2019	Operations & Plans Department	The TWG has been established and the first meeting conducted
6	NATO Aircraft Bomb recognition training for DMAC ROs and IPs.	Sep 2019 – Mar 2020	Operations	
7	Conduct a study on MEIFCS (Needs, Achievements).	June – July 2019	Operations	In recent MAPA OPS review workshop it was decided to stop MEIFCS and cover the remaining district with only NTS
8	Develop a list of detectors available within MAPA with all specifications including detection capabilities.	May-Aug 2019	Operations	Ongoing - 70% completed
9	To Develop the deminer database and collecting the required information from the IPs	May – Dec 2019	Operations	Initial list has been sent by 7 IPs follow-up with other IPs is ongoing
10	Modification of MDU database in order to include all MDUs specifications and other required information.	April-Sep 2019	Operations in coordination with IPs	Information gathering from the IPs is ongoing

S. #	Activity	Time Frame	Responsible Department	Progress Tracking
11	Confirmation assessment of remaining unconfirmed hazardous areas as well as conducting NTS on ERW sites initially surveyed based on the request of national security council (NSC).	April 2019 - March 2020	Operations in coordination with regional offices	Ongoing
12	Review AMAS survey chapter for reflecting VOIED issue.	May-June 2019	QM & operations	
13	Conduct a study on existing AV minefields and its linkage to development.	May 2019 – Mar 2020	Plans department with support by Operations	
14	Develop the liability policy for MAPA.	April-June 2018	Quality Management	

### Mine Action Livelihoods Survey and Post Demining Impact Assessment (PDIA):

The main objective of the Mine Action Livelihoods Survey and Post Demining Impact Assessment (PDIA) is to better understand the mine action impact on livelihoods and development of communities that have been cleared of mines/ ERW and how to further enhance the positive impact of mine action intervention to the communities.

DMAC plans to conduct the following activities during 1398:

S-No.	Activity	Deadline	Progress tracking
1	DMAC, in close coordination with ANDMA, will conduct the Mine Action Livelihoods Survey in 12 communities of Kapisa Province.	June through September 2019	The plan has already been prepared and soon will be conducted
2	PDIA will be conducted on 10 percent of the cleared hazardous areas of 1397, which will cover about 85 cleared contaminated areas, in around 14 provinces located in six regions of Afghanistan.	April through September 2019	The PDIA has already been started and so far, completed in 5 provinces

### 2.1.3 Quality Assurance and Quality Control

The aim of quality management (QM) is to provide confidence to the beneficiaries, funding bodies, mine action contractors and the Government of Afghanistan that mine action quality requirements are met, and that cleared land is indeed safe for use. QM consists of three complementary components: accreditation, monitoring and post-clearance inspection.

As per the QM principles, the QM department plays an important role in order to maintain the stakeholders' satisfaction through the provision of quality services. The main functions of the QM department are: managing and maintaining the Afghanistan Mine Action Standards (AMAS); processing accreditation of mine action organizations (humanitarian and commercial) and projects (operational and organizational), managing and undertaking monitoring and quality control of mine action activities, operations and services; investigating demining incidents; managing and maintaining internal quality management systems of DMAC, managing and maintaining DMAC internal documents including standard operating procedures and processes; conducting internal audit and measuring processes; developing the DMAC balanced scorecard reports; and developing QM related policies.

DMAC Quality Management (QM) department will undertake the below activities in 1398.

*Table 5: QM Priorities/activities in 1398*

S/N	Activity	Frequency/ Target date	Progress Tracking
1	Analysis of QA findings to discuss during the operations workshop.	April 2019	Done
2	Amend the current AMAS for EOD.	Sep 2019	
3	Develop a risk management strategy for DMAC and MAPA.	August 2019	Risk Management Framework is already developed
4	Develop a Liability Policy.	Dec 2019	
5	Revision a QA completion form.	May 2019	Done
6	Establish a QM working group.	April 2019	Done
7	Amend the current AMAS for QM and develop a new AMAS for a Quality Management System (QMS) in Mine Action and further review in order to add the minimum frequency for QA visits.	Oct 2019	
8	Monitor DMAC performance through DMAC BSC.	Quarterly	On going
9	Conduct 2,200 QA monitoring visits and QC of mine action projects and teams.	Throughout the Year	On going

### 2.1.4 Information Management

The Management Information System (MIS) department manages the Information Management System for Mine Action (IMSMA) database for the MAPA. This database uses IMSMA as a centralized data entry system which has been adapted to suit the operations, systems and procedures used in

Afghanistan. IMSMA provides the baseline for the planning and coordination of mine action operations and acts as the master database for all mine action information in Afghanistan. The MIS section also produces standard topographical and hazards-based mapping for the MAPA, and the Geographical Information System (GIS) section collects, manages and maintains all types of geospatial data from various sources to analyse mine action data and uses remote sensing technology to visualize and analyse contaminated areas databased on satellite imagery.

The following activities will be carried out by the DMAC Management Information Systems (MIS) Department during 1398.

*Table 6: Information Management activities in 1398*



S#	Activity	Deadline	Progress Tracking
1	Work with Geneva International Cooperation for Humanitarian Demining (GICHD) for more accurate population data.	Dec 2019	
2	IMSMA cloud-based data storage and online backup system.	Sep 2019	Completed. 3 Different Backup system for IMSMA data storage
3	WHO-standards data collection and reporting system for VA.	May 2019	IMSMA VA data collection template updated
4	Purchase of GIS software/shapefiles for DMAC MIS.	June 2019	Working with GICHD to purchase the GIS software. Land-Scan data purchased. Shapefile issue still ongoing.
5	Preparation for implementation of the latest version IMSMA (Core) in Afghanistan.	March 2020	
6	Provision of Cloud based online backup system for MIS.	June 2019	IMSMA data is now stored in G-Suite drive as cloud storage
7	<u>Digital Reporting/Data analysis system</u> : Develop a mobile application for field data collection, including GIS data. MAPA will be able to monitor field activities using geotag photos and geolocation information. The MAPA will have a web-based data management and administration portal and a cloud-based data warehouse.	March 2020	TOR update and shared with GICHD. GICHD team is working on this .
8	<u>Apply the latest data analysis/ reporting technology in the MAPA</u> : Implementation of the latest data analysis/ reporting technology in the MAPA to provide advanced data management, query, processing and reporting systems designed to maximize data assets, information and business intelligence.	March 2020	TOR update and shared with GICHD. GICHD team is working on this

S#	Activity	Deadline	Progress Tracking
9	Conduct data quality improvement meetings with IPs, ROs and UNMAS	August 2019	1 Meeting conducted (23-24 June) Second is on 7-8 July

## 2.2 Survey and Clearance

### 2.2.1 Survey

Graph 4: Countrywide status of MEIFCS survey and Non-Technical Survey

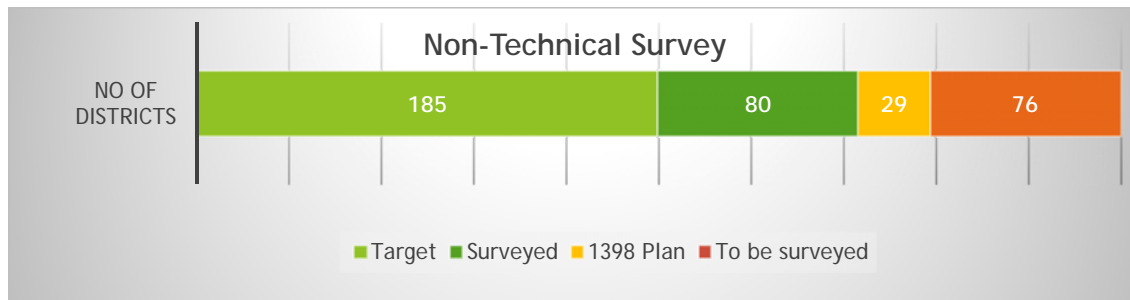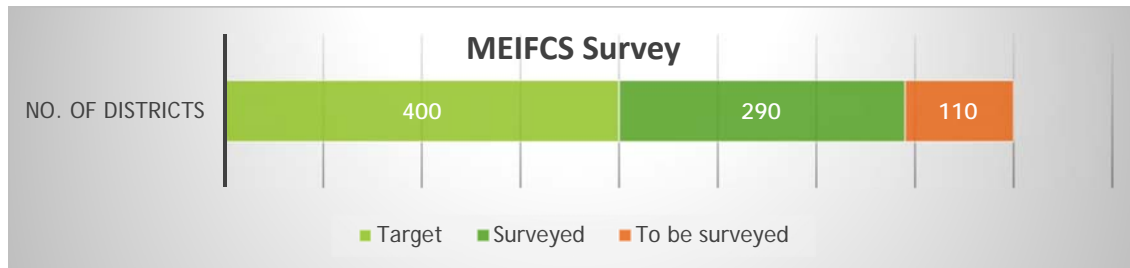

Survey plays a fundamental role in identifying the scope of the current mine and ERW problem. The MAPA plans to conduct the following two surveys in 1398:

#### **Mine/ERW Impact Free Community Survey (MEIFCS)**

As part of Afghanistan's extension request to the APMBC, DMAC launched a nationwide mine/ERW Impact Free Community Survey (MEIFCS) in 2012 in which all communities are to be surveyed.

The MEIFCS includes non-technical survey, destruction of spot ERW, and the provision of M/ERW RE messages to each community visited.

#### *Summary of MEIFCS progress to date:*

- A goal of 400 districts across the country was initially planned in 2012.

- 290 districts have been completed before 1398, but due to unavailability of funding no districts planned so far for 1398.
- 110 districts remain to be surveyed. Most of the remaining districts are in hard to access areas due to security concerns.

*Funding status:*

No funds are available to conduct MEIFCS in 1398<sup>8</sup> at this stage.

There is a need to survey 412 impacted communities and 8,951 communities with unknown contamination status in 110 districts where the impact is unknown. Based on experience, an increase of 100 to 140 per cent in the number of communities to be surveyed is expected, since many communities are not included in the national gazetteer.

**Non-Technical Survey (NTS):**

NTS is the process of information gathering through which evidence-based decisions are made about newly reported and previously recorded hazardous areas.

As part of the NTS operations in kinetic engagement sites, the primary focus of the NTS is to capture any possible contaminated areas due to kinetic operations in the effected districts.

*Summary of NTS:*

- Districts part of kinetic engagement planned for NTS: 185
- Districts completed so far: 80
- Districts planned for 1398 for survey: 29
- Districts remaining for future years: 76

Comprehensive information on the extent and impact of all contamination resulting from the post-2001 conflict in Afghanistan is not always readily available. The MAPA partners aim to continue efforts to conduct surveys of unrecorded or changing areas to ensure that planning and prioritization of clearance by the DMAC are possible and based on new and comprehensive information.

*Funded:*

DMAC plans to conduct NTS in 29 districts in 1398 funded by PM/WRA. This project is already awarded to Mine Clearance Planning Agency (MCPA) and will be implemented in six regions (Central, East, North, Northeast, South & South East) from April 2019 to March 2020.

*Unfunded:*


There are 76 districts where there is a need to conduct NTS operations; however, there are no funds available and the security situation in some of these districts is not stable.

---

<sup>8</sup> Refer to the DMAC website ([www.dmac.gov.af](http://www.dmac.gov.af)) to see the list of targeted MEIFCS projects for 1398.


## 2.2.2 Clearance (explosive hazard reduction)

Graph 5: 1398 Areas targeted, funded and gaps as of March 2019

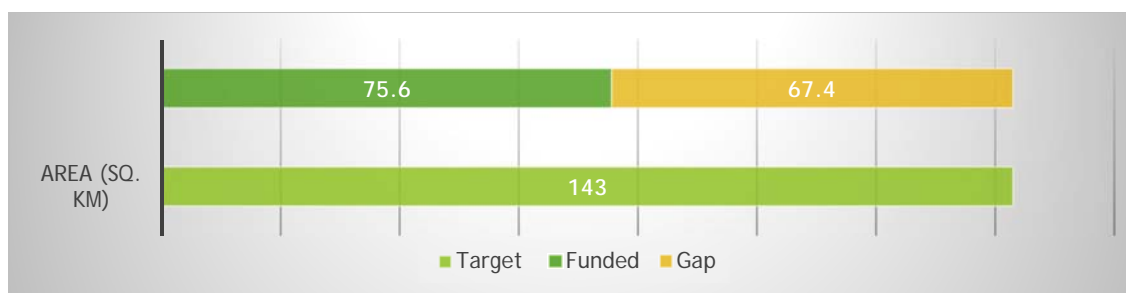

As per the MBC workplan, the programme needs to release 143 sq. km of known contamination in 1398. The breakdown of types of areas to be released as per the MBC workplan is shown in the graph below.

Graph 6: Percentage of targeted areas for 1398

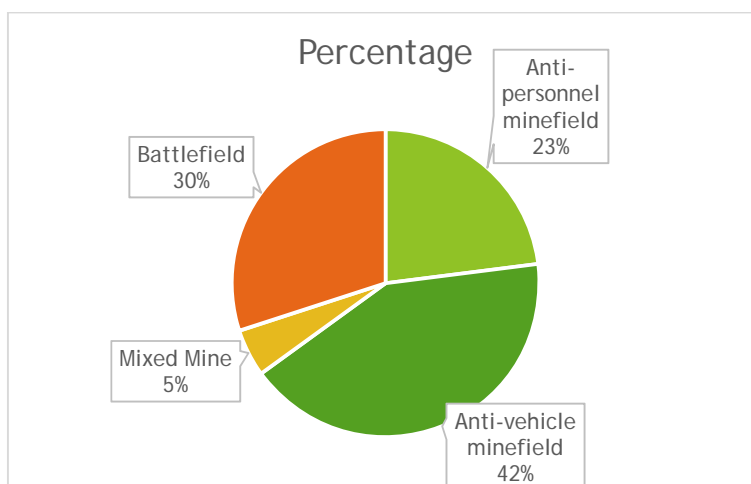

The funding situation for the programme has improved this year compared to 1396. As of month of July which equivalent to the month 4<sup>th</sup> of 1398 donors have committed to clear 75.6 sq. km of land with confirmed funds and 18.7 sq. km area with funds pledged (unconfirmed) so far. Considering the confirmed funds, this covers 53 per cent of the 143 sq. km targeted in the 1398 MBC workplan<sup>9</sup>. The breakdown of confirmed/committed projects, funding channels and donors are detailed below.

### **Voluntary Trust Fund (VTF):**

The VTF contributions for 1398 are from the following donors<sup>10</sup>: United Kingdom (DFID), Canada, Belgium, Japan, Finland and Netherlands (Dutch). Below is a table of VTF funded grants as of July 2019:

<sup>9</sup> refer to the DMAC website ([www.dmac.gov.af](http://www.dmac.gov.af)) to see list of targeted demining projects for 1398 awaiting funds.

<sup>10</sup> Some of the donors have contributed in funding of projects started in 1397 and would continue in 1398 and some contributed in 1398 project that may continue during 1399, we only reflected the size of area that would be cleared during 1398 in above table.

Table 7: VTF funded projects for 1398, as of July 2019

Project Name	Province	Project fund Status	Start Date	End Date	Area of Confirm Fund	Area of Pledged fund	Channel	Donor	Agency
Baghlan Demining Project-22/C	Baghlan	Confirm	1/Jan/18	10/Jan/19	679,942		VTF	UNMAS	ATC
DDG Parwan and Bamyan VTF Demining Project-1398	Bamyan, Parwan	Confirm	3/Apr/19	3/Dec/19	711,251		VTF	UNMAS	DDG
HT VTF Baghlan Demining Project-1398	Baghlan	Confirm	19/Feb/19	31/Jan/20	1,227,400		VTF	UNMAS	HT
AFG/UNMAS/21215/2018/010	Farah	Confirm	10/Oct/18	30/Nov/19	1,433,741		VTF	UNMAS	ATC
AFG/UNMAS/21215/2018/012	Kandahar	Confirm	2/Oct/18	31/Jul/19	3,245,377		VTF	UNMAS	DAFA
ATC Takhar and Baghlan VTF Demining Project-1398	Baghlan, Takhar	Confirm	15/Mar/19	15/Dec/19	1,497,093		VTF	UNMAS	ATC
DAFA VTF Hirat Demining Project-1398	Hirat	Confirm	1/Jun/18	31/Mar/20	3,450,533		VTF	UNMAS	DAFA
HT VTF Maydan Wardak Demining Project-1398	Maydan Wardak	Confirm	1/Mar/19	31/Dec/19	1,094,503		VTF	UNMAS	HT
MCPA/DAFA VTF Nimroz Demining Project-1398	Nimroz	Confirm	15/Jun/19	31/Mar/20	2,052,052		VTF	UNMAS	MCPA
OMAR VTF Logar Demining Project-1398	Logar	Confirm	05-May-19	13-Feb-20	4,132,779		VTF	UNMAS	OMAR
Provision of Regional Mine Action Quick Response Capacity in Afghanistan	Balkh, Ghazni, Hilmand, Paktika	Confirm	1/Jan/19	28/Feb/20	1,601,184		VTF	UNMAS	HT
MCPA/DAFA VTF Demining Project-2019	Zabul	Confirm	4/Jun/19	31/Dec/19	6,517,895		VTF	UNMAS	MCPA
Baghlan Demining Project-06	Baghlan	Pledged				693,042	VTF	UNMAS	
Kunar Demining Project-03	Kunar	Pledged				3,633,469	VTF	UNMAS	
Nangarhar Demining Project-03/I	Nangarhar	Pledged				713,500	VTF	UNMAS	
Nangarhar Demining Project-03/J	Nangarhar	Pledged				3,247,043	VTF	UNMAS	
Paktya Demining Project-03/C	Paktya	Pledged				341,568	VTF	UNMAS	
Paktya Demining Project-03/E	Paktya	Pledged				575,501	VTF	UNMAS	
Paktya Demining Project-06	Paktya	Pledged				786,605	VTF	UNMAS	
<b>Total</b>					<b>27,643,749</b>	<b>9,990,728</b>			

**Bilateral Projects:**

Projects that receive funds through bilateral donors are divided into two subcomponents: USDoS funded projects (NOFOs and unsolicited) and other bilateral.

- a. 1398 Notice of Funding Opportunities (NOFOs) and unsolicited projects by PM/WRA

Below are projects funded by PM/WRA for the year 1398. It is worth mentioning that all of these NOFOs were awarded during 1397 due to the grants process the projects started in 1398, while few NOFOs also started in 1397. The list of PM/WRA projects is shown in the below table.



Table 8: PMWRA funded NOFO projects for 1398 as of July 2019

Project Name	Province	Project fund Status	Start Date	End Date	Area of Confirm Fund	Area of Pledged fund	channel	Donor	Agency
Badakhshan Demining Project-03/D	Badakhshan	Confirm	1/Jan/18	31/Dec/19	313,704		Bilateral	USDoS	FSD
Baghlan Demining Project-03/F	Baghlan	Confirm	1/Jul/18	30/Jun/19	146,781		Bilateral	USDoS	DDG
Nangarhar Demining Project-06	Nangarhar	Confirm	1/Jul/18	30/Jun/19	106,054		Bilateral	USDoS	DDG
NOFO Project-16 Panjshir	Panjsher	Confirm	1/Jul/18	30/Jun/19	242,453		Bilateral	USDoS	DDG
Panjshir Demining Project-05/B	Panjsher	Confirm	1/Jul/18	30/Jun/19	389,062		Bilateral	USDoS	DDG
Parwan Demining Project-14	Parwan	Confirm	1/Jul/18	30/Jun/19	126,053		Bilateral	USDoS	DDG
HT/DACAAR VTF Kandahar Demining Project-1398	Kandahar	Confirm	1/Jul/19	31/Mar/20	1,561,424		Bilateral	USDoS	HT
Kabul Demining Project-19/C	Kabul	Confirm	1/Apr/18	31/Jul/19	1,280		Bilateral	USDoS	HT
Kapisa Demining Project-02	Kapisa	Confirm	1/Apr/18	31/Jul/19	356,237		Bilateral	USDoS	HT
Logar Demining Project-01 (AT)	Logar	Confirm	1/Apr/18	31/Jul/19	191,378		Bilateral	USDoS	HT
Maydan Wardak Demining Project-05/B	Maydan Wardak	Confirm	25/Sep/17	24/Sep/19	182,796		Bilateral	USDoS	DAFA
Nangarhar Demining Project-05/G	Nangarhar	Confirm	25/Sep/17	24/Sep/19	635,900		Bilateral	USDoS	DAFA
NOFO Project 26 Panjsher-Nangarhar	Nangarhar, Panjsher	Confirm	1/Jul/19	30/Jun/20	1,322,426		Bilateral	USDoS	HT
NOFO Project-20 Baghlan and Laghman	Baghlan, Laghman	Confirm	1/May/19	30/Apr/20	3,527,912		Bilateral	USDoS	HT
NOFO Project-21 Baghlan and Kunar	Baghlan, Kunar	Confirm	17/Jun/19	30/Apr/20	6,127,902		Bilateral	USDoS	ATC
NOFO Project-22 Kandahar	Kandahar	Confirm	20/Jun/19	19/Jun/20	5,627,206		Bilateral	USDoS	ATC
NOFO Project-23 Samangan-Balkh-Khost	Balkh, Khost, Samangan	Confirm	1/Jul/19	30/Jun/20	3,039,519		Bilateral	USDoS	HT
NOFO Project-24 Maydan Wardak-Nimruz	Maydan Wardak, Nimroz	Confirm	1/Jun/19	31/May/20	3,340,642		Bilateral	USDoS	DAFA
NOFO Project-25 Kapisa-Baghlan-Khost	Baghlan, Kapisa, Khost	Confirm	1/May/19	30/Apr/20	1,383,563		Bilateral	USDoS	DAFA
Parwan Demining Project-08/A	Parwan	Confirm	1/Apr/18	31/Jul/19	219,212		Bilateral	USDoS	HT
Takhar Demining Project-03/A	Takhar	Confirm	25/Sep/17	24/Sep/19	963,424		Bilateral	USDoS	DAFA
Hirat Demining Project-03	Hirat	Pledged				1,410,437	Bilateral	DOS	ATC
Hirat Demining Project-04	Hirat	Pledged				2,669,460	Bilateral	DOS	ATC
Kabul Demining Project-19/G	Kabul	Pledged				414,966	Bilateral	DOS	AREA
Kunduz Demining Project-04	Kunduz	Pledged				860,781	Bilateral	DOS	OMAR
Kunduz Demining Project-04/A	Kunduz	Pledged				149,911	Bilateral	DOS	OMAR
Logar Demining Project-01 (AT)/E	Logar	Pledged				1,353,000	Bilateral	DOS	HT

Project Name	Province	Project fund Status	Start Date	End Date	Area of Confirm Fund	Area of Pledged fund	channel	Donor	Agency
Nangarhar Demining Project-03/H	Nangarhar	Pledged				194,157	Bilateral	DOS	MDC
Nangarhar Demining Project-05/B	Nangarhar	Pledged				195,989	Bilateral	DOS	MDC
Panjshir Demining Project-05/A	Panjshir	Pledged				126,956	Bilateral	DOS	AREA
Panjshir Demining Project-05/G	Panjshir	Pledged				449,000	Bilateral	DOS	AREA
Takhar Demining Project-08/C	Takhar	Pledged				934,098	Bilateral	DOS	MDC
<b>Total</b>						<b>29,804,927</b>			

**b. Other Bilateral Funded Projects:**

The list of clearance projects funded or to be funded by donors through bilateral channel other than PM/WRA is listed in below:

*Table 9: Projects funded by different donors for the year 1398 as of July 2019*

Project Name	Province	Project fund Status	Start Date	End Date	Area of Confirm Fund	channel	Donor	Agency
DDG DANIDA Demining Project-2019	Kabul	Confirm	1/Jan/19	31/Dec/19	330,956	Bilateral	DANIDA	DDG
HT Finland Demining Project-1398	Baghlan, Parwan, Samangan, Takhar	Confirm	1/Jan/19	31/Dec/19	2,333,524	Bilateral	Finland	HT
Hilmand AIM Clearance Project-01	Hilmand	Confirm	1/Jan/19	30/Jun/19	841,364	Bilateral	Germany	HT
HT GFFO MC Demining Project 2019-2020	Baghlan, Balkh, Parwan, Samangan	Confirm	1/Jan/19	30/Jun/20	2,799,873	Bilateral	Germany	HT
Kandahar Demining Project-04 AT/E	Kandahar	Confirm	1/Jan/19	31/Dec/19	1,351,607	Bilateral	Irland	HT
AREA GAGP Demining Project-1398	Nangarhar	Confirm	1/Mar/19	31/Jan/20	323,606	Bilateral	Japan	AREA
HT AAR Demining Project 1398	Baghlan	Confirm	1/Jun/19	30/Dec/19	39,394	Bilateral	Japan	HT
OMAR GAGP Demining Project-1398	Kapisa, Parwan	Confirm	27/Feb/19	26/Feb/20	594,442	Bilateral	Japan	OMAR
HT AIM Survey + Clearance project 1397/1398	Hilmand	Confirm			19,357	Bilateral	Netherlands	HT
HT RNG Demining Project 2019	Baghlan, Kabul, Samangan	Confirm	1/Jan/19	31/Dec/19	1,379,261	Bilateral	Netherlands	HT
Kandahar Demining Project-01/H	Kandahar	Confirm	1/Jul/19	30/Jun/20	1,375,052	Bilateral	Norway	HT

Project Name	Province	Project fund Status	Start Date	End Date	Area of Confirm Fund	channel	Donor	Agency
FSD PATRIP Demining Project-2019	Badakhshan	Confirm	1/Jan/19	31/Dec/19	151,594	Bilateral	PATRIP	FSD
DDG SIDA Demining Project-2019	Balkh, Samangan	Confirm	1/Jan/18	31/Dec/21	422,031	Bilateral	SIDA	DDG
HT CSSF Demining Project-1398	Baghlan, Balkh, Logar, Samangan	Confirm	1/Apr/19	31/Mar/20	6,284,727	Bilateral	UK-CSSF	HT
<b>Total</b>					<b>18,246,788</b>			

### *Funded*

Update in July 2019: With the confirmed funding for clearance, the following will be achieved during 1398:

- 581 contaminated areas/hazards will be released;
- 75.6 sq.km of land will be released;
- 187 communities will be released;
- 16 districts will be released; and
- 399,942 people will benefit from the clearance.

The detailed list of available and committed funds for demining projects is in Annex A of this work plan.

### *Unfunded:*

According to the extension request, the following needs to be funded during 1398:

- 456 contaminated hazards;
- 67.4 sq. km of contaminated land;
- 149 mine/ERW impacted communities;
- 27 mine/ERW impacted districts; and
- 479,286 people would benefit from the above clearance.

### **Firing Ranges:**

The Firing Range project which started in 2013 ended in May 2018 due to a funding shortfall. DMAC will keep advocating for continued funding until the remaining firing ranges are cleared.

The Post Demining Impact Assessment (PDIA) of the cleared firing ranges was completed during June to September 2018. Meanwhile, DDG conducted fresh NTS of the 5 firing ranges in Bamyan. As a result, one firing range has been entirely cancelled and others reduced from 219 Sq. Km to 39 Sq. Km. This activity was funded by UNMAS VTF.

A concept note was submitted to New Zealand for clearance of the surveyed firing ranges in Bamyan.


### ***Stockpile destruction***

In 1398, HALO Trust will deploy 17 Weapons and Ammunition Disposal (WAD) one (WAD/ MST) MoD support team, eight conventional weapons destruction teams, two WAD survey teams, and will conduct the following activities to reduce the risk of stockpile scattered ammunition in the country:

S#	Activity	Deadline	Progress Tracking
1	Survey 600 villages to determine the location of ammunition bunkers	1 <sup>st</sup> Apr 2019 – 31 <sup>st</sup> Mar 2020	170 villages surveyed so far
2	Destroy 680 metric tons of unserviceable ammunition.	1 <sup>st</sup> Apr 2019 – 31 <sup>st</sup> Mar 2020	305 MT of unserviceable ammunition destroyed so far
3	Convene Ammunition Working Group (AWG) meetings to increase involvement in the planning and implementation of stockpile destruction.	1 <sup>st</sup> Apr 2019 – 31 <sup>st</sup> Mar 2020	

## 2.3 Victim Assistance

Graph 7: Victim assistance fund and gaps for 1398

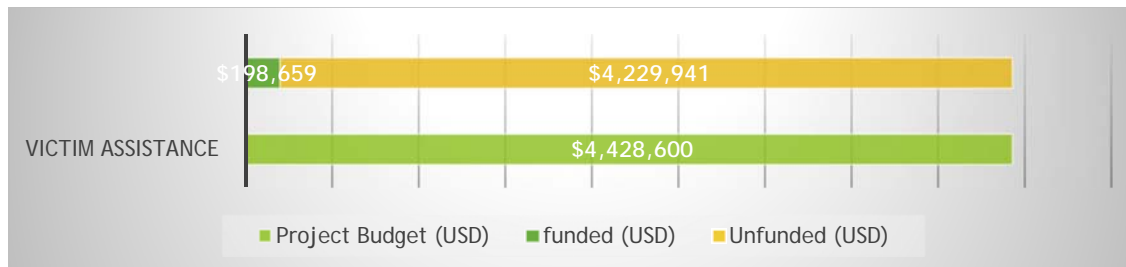

The ongoing conflict in Afghanistan continues to take a severe toll on the civilian population killing and injuring an alarming number of civilians and straining the already taxed and fragile health system. The nature of the conflict, which includes widespread use of improvised explosive devices, has claimed the lives of over 32,000 and left over 59,500 injured since 2009<sup>11</sup>. The large number of survivors of ground engagements, suicide attacks, explosive contaminated areas and other conflict-related threats against civilians are often left with life-altering injuries and disabilities. They require access to basic healthcare and more specialized services including physical therapy and psychosocial support.

Table 10: Victim Assistance activities during 1398.

Activity Area	Activity	Deadline	Progress Tracking
Information Management	Support MMD with testing and implementing a central database within the state ministry for housing data on victim assistance services provided by all government and civil society actors in Afghanistan (UN, national and international NGOs). Provide technical advice on troubleshooting system issues.  The database is a critical tool for the state ministry to: 1) analyse services being provided and determine gaps; and 2) prioritize and plan services for greater effectiveness.	Sep 2019	The database is under review, with GICHD to apply new fields for wider disability

<sup>11</sup> Afghanistan Protection of Civilians in Armed Conflicts Annual Report 2018, UNAMA

Activity Area	Activity	Deadline	Progress Tracking
National Disability Strategy & Workplan	<p>Provide technical support to the state Ministry for Martyrs and Disabled affairs for the continued development of a national disability strategy (including assistance for victims of landmines and ERW), in coordination with all relevant government bodies.</p> <p>An accompanying workplan and budget will be developed to highlight needs, responsibilities and funded vs. underfunded activities. This will be done to the extent that this process leads to DMAC being assigned responsibilities which require additional funds, this portfolio submission will be amended.</p>	June 2019	70 % of work is completed
Physical Accessibility	Identification of public places/buildings for ramps construction in consultation with relevant ministries and Service 500 public buildings in 17 provinces to enable access to persons with disabilities.	Throughout 1398	Advocacy is conducted to the Ministerial Council and they promised to construct ramps.
Economic Reintegration	<p>Data analyzing of PwD for 700 small business creation in coordination with MMD.</p> <p>Support to 700 persons with disabilities to regain livelihoods through small and medium enterprise.</p>	Throughout 1398	
Advocacy and awareness	Translation and printing of books and awareness materials to increase disability awareness;	Throughout 1398	VA messages are shared with MoPH – Vaccination Dep to add to their materials.
Socio-economic reintegration of Victim Deminers	To assist ex-deminers that have been injured during demining operations in reintegrating into society, both socially and economically.	Throughout 1398	
Physical Rehabilitation	Continue support to established fixed and mobile physical rehabilitation clinics providing services, such as physiotherapy, prosthesis and orthotic services, as well as sensitisation on the rights of persons with disability.		Two centres in Paktya and Farah are funded by USAID
Inclusive Education for Children with Disability CwD	Production of education materials, tools and training to ensure inclusive education for persons with disabilities. Collecting data about CwD/ Mine & ERW victims and developing distribution plan in consultation with MoE.	Throughout 1398	
First Aid training to	Identify impacted community and collect data about Community Health Workers (CHW) and supervisors/Trainers from MoPH.	Throughout 1398	Project has not been fund yet

Activity Area	Activity	Deadline	Progress Tracking
Community Health Workers of MoPH	Conduct Training of Trainers (ToT) of trauma management for CHW supervisors/trainers in consultation with MoPH.		
Advocating Across Sectors	An Advocacy campaign by VA and Disability stakeholders will get underway by Dec 2019. Campaign will reach across sectors.	Dec 2019	
Increasing Coordination	UN and civil society are increasing coordination, new working group will be established under Inter-ministerial committee for disability meetings. MMD to act as a coordination body.	Throughout 1398	ToR for Inter-ministerial Committee has been drafted, MoUs between MMD and other Ministries have been signed, Inter-Ministerial Action plan for coordination has been developed.
Connecting with Global Efforts	- MAPA donor workshop. 12 <sup>th</sup> session of the conference of states Parties to the UN DRPD. - Exposure visit from Iran MRE and VA activities.	July 2019	Donor Workshop participated; the Exposure visit has been conducted.

The Afghan context presents challenges in fulfilling the needs of persons with disabilities (regardless of the cause of the disability) including ensuring that women and persons living in rural communities can access care. Although there is a lack of precise information on the number of persons with disabilities in the country, some surveys conducted by various organizations in the past suggest that around 800,000 people are living with disabilities in the country, that is equivalent to 2.7 per cent of the population. Access to care is currently inadequate; an estimated 90 per cent of the Afghan population live more than 100 km away from a rehabilitation centre<sup>12</sup>; 20 provinces out of 34 have no prostheses and orthoses service providers and are lacking female health service providers and rehabilitation professionals. Increased government capacity is needed to properly care for mine and ERW survivors and ensure inclusive education for children with disabilities.

The ongoing war and the presence of mines, ERW and IMs in the country increase the prevalence of disability. MAPA is committed to continue to help victims of conflicts and maintaining its advisory capacity at the Ministries of Martyrs and Disability Affairs, Public Health and Education (MMD, MoPH, and MoE).

The objective of victim assistance within the MAPA is to provide technical assistance to the State Ministry for Martyrs and Disabled Affairs (MMD) to increase the capacity of the ministry to serve the

<sup>12</sup> Financial Access to Rehabilitation Services in Afghanistan in 2016, HI.

martyrs and disabled population (including victims of landmines and ERW). The table below outlines the activities to be completed in 1398 to achieve this objective.

**Funds are confirmed for the following projects:**

*Table 11: List of VA projects with fund confirmed/committed for 1398*

Project/ Activity <sup>13</sup>	Target Group	Funding source	Estimated Number of beneficiaries	Est. start date	Est. completion date	Remarks	Status
Electronic Registration of M&D	<i>Persons with disabilities</i>	VTF	<i>300,000 Persons with disabilities</i>	Aug-19	July-2020		
Total			<b>300,000</b>				

**Funded:**

*The following is the only funded project for victim assistance for 1398 (2019):*

- Electronic registration of 300,000 martyrs and persons with disabilities which will work towards the E-governance goal of the GoIRA and to speed up the service delivery process for war victims in a transparent process.

**Unfunded:**

*The following projects are designed based on the needs of persons with disabilities including victims of Mine and ERW. Still, there is not a confirmed budget for the projects, but if funding becomes available, the projects can be implemented during 1398 (2019 – 2020):*


- Physical Accessibility – US \$385,000
- Economic Reintegration – US \$700,000
- Advocacy and awareness – US \$60,000
- Inclusive Education for CwD – US \$100,000
- Physical Rehabilitation – US \$1,200,000
- Socio-economic reintegration of Victim Deminers – US \$1,018,000
- First Aid training to Community Health Workers of MoPH – US \$365,600

<sup>13</sup> Refer to the detailed list of VA proposed projects at the DMAC Website at [www.dmac.org](http://www.dmac.org).



## 2.4 Mine and Explosive Remnants of War Risk Education

Graph 8: MRE funding and gaps for 1398

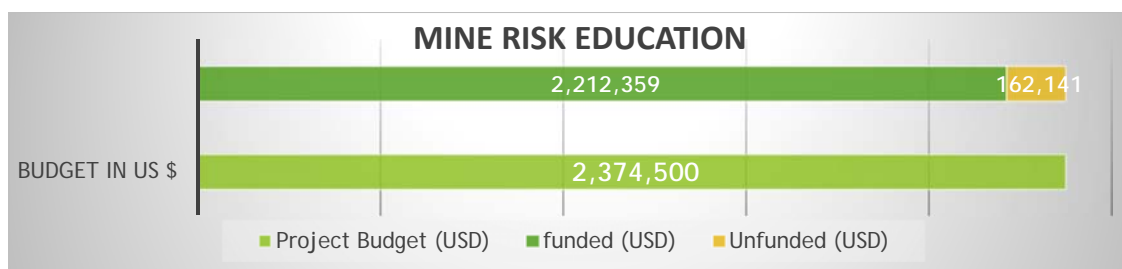

Afghanistan remains heavily affected by landmines and ERW which continue to threaten Afghan lives and limbs. Landmine and ERW contamination affect an estimated 2.5 million people living in close proximity to landmines; people on the move, including refugees returning to their homeland (returnees), Internally Displaced Persons (IDPs), who are either fleeing due to conflict or returning post-conflict and people who travel within their communities for day to day needs such as visiting marketplaces, hospitals, relatives, or attending ceremonies; and children playing or going to school.

The 2018 UNAMA Protection of Civilians Report indicates that 87 per cent of civilian casualties due to ERW are children who, in many cases, were killed or injured because they touched explosive remnants of war they found, played with the device or even carried it home<sup>14</sup>.

Mine/ERW Risk Education (RE) is vital to educate affected communities on the dangers of mines/ERW. Mine/ERW RE ensures that communities are aware of the risks of mines, unexploded ordnance and/or abandoned munitions and are encouraged to behave in ways that reduce the risk to people, property and the environment. The objective is to reduce the risk to a level where people can live safely and to recreate an environment where economic and social development can occur free from the constraints imposed by landmine contamination.<sup>15</sup>

*Funded:*

- a. The UNMAS VTF will fund:

Table 12: List of MRE projects with UNMAS VTF funding confirmed/committed for 1398

Activity Area	Activity	Deadline	Progress tracking
MRE through Mass Media	To deliver mine/ERW risk education messages through two popular TV channels (TOLO and SHAMSHAD) with extensive coverage in both Pashto and Dari languages for 120 days throughout a year. The messages will be as drama dialogue and ideally the narration by famous faces of the country i.e. popular cricket players	Apr 2019 – Mar 2020	Script translated to local languages, approved and shared for filming.
Direct Risk Education for returnees in Encashment Centers (EC), Transit Centers (TC) and Zero Points	To Conduct direct Risk Education for returnees in Encashment Centers (EC), Transit Centers (TC) and Zero Points (ZP)	Apr-Dec 2019	Ongoing smoothly in Kabul, Nangarhar, Hirat,

<sup>14</sup> United Nations Assistance Mission to Afghanistan. (2018). Retrieved from <https://unama.unmissions.org/protection-of-civilians-reports>

<sup>15</sup> Mine Risk Education. (n.d.). Retrieved from <http://www.mineaction.org/issues/education>.

Activity Area	Activity	Deadline	Progress tracking
(ZP)			Nimroz and Kandahar.
Speaking Books	To Design and Print 7,500 MRE T- Book for 7,500 schools located in 20 provinces in the most impacted areas/provinces. To provide MRE Speaking Books ToT to 115 Child Protection Officers (CPOs) of MoE from 34 provinces in Kabul city who will then provide MRE Peaking Books ToT to 7,500 school teachers of 20 high impacted provinces through 115 CPOs of MoE.	Apr-Dec 2019	Proposal developed and shared with Donor.
Causality Data Collection and MRE by ARCS	In the period of one year, conduct 12,960 MRE sessions for 324,000 female and male participants in 30 provinces with the use of 30 MRE mobile teams consisting of couple teams. The teams will also collect civilian victim data from all available sources such as health clinics, communities (CDCs), and community members which then will be entered into the IMSMA system. Finally, the teams will refer the mine / ERW victims to service providers based on referral guide information.	July 2019 – June 2020	Proposal developed and shared with donor.
Three-digit Hotline	To create a free, short and easy hotline contact number to enable DMAC to receive mine/ERW and AIM issues in a timely manner.	May 2019 – Apr 2020	Proposal developed and shared with donor.

b. Bilateral Funds:

*Table 13: List of MRE projects with Bilateral funding confirmed/committed for 1398*

Activity Area	Activity	Deadline	Progress Tracking
Community Based MRE	Provision of RE to most at-risk groups, including but not limited to, community members living in proximity of mine/ ERW contaminated areas, IDPs, Nomads (Kuchies) through MRE sessions in the communities.	Through-out the year	The CB MRE is ongoing by AAR Japan, HALO Trust, OMAR and DDG countrywide.

*Unfunded:*

*Table 14: List of MRE projects currently unfunded for 1398.*

Activity Area	Activity	Deadline	Progress Tracking
M/ERW RE ToT to CPOs and teachers of MoE in all provinces and installation of	Providing M/ERW RE refreshment training to 120 CPOs of MoE and through the CPOs to 7,500 school teachers in high impacted communities in 20 provinces.  Installation of 7,500 billboards in 7,500 schools of 20 provinces in most affected communities.	Through-out the year	Meetings held with the UNICEF and NRC

MRE Billboards			and project discussed
Nationwide KAP survey	The purpose of the KAP survey is to assess the impact and outcome of the Risk Education on the communities and to understand on how and to which extent the MRE resulted in behaviour change of the affected communities.	October-December 2019	
The evaluation of the MRE in 725 Schools of Afghanistan	The purpose of this evaluation is to measure the effectiveness of the existing mechanism for the implementation MRE in the schools by conducting interviews with teachers, evaluate the availability of MRE trained teachers in schools, evaluating the school curriculum Risk Education messages, measuring the duration of time given by schools management for MRE sessions, measuring the interest and understanding of pupils from mine/ERW risk and test their behaviour change.	September-December 2019	

## 2.5 Gender & Diversity Mainstreaming:

Women, girls, boys and men of different ages and backgrounds have distinct roles and responsibilities within communities.

Mine action aims to reduce the human, social, economic and environmental impact of explosive remnants of war (ERW) and landmines. However, this can be fulfilled only by understanding the implication of any action on different groups of people. In mine-affected areas, each group and individual are affected differently by contamination, and each holds different views on the problem. The needs, constraints, capacities and resources of women, girls, boys, and men needs to be analyzed to ensure effective, sustainable and inclusive mine action. In addition, gender and diversity analysis and programming lead to more productivity, better working environment and higher quality services.

The principle of non-discrimination is at the core of internationally recognized human rights standards and, in the context of mine action, is reflected in the Anti-Personnel Mine Ban Convention.

DMAC Gender and Diversity (G&D) department, with support of the IPs, plan to achieve the following during 1398:

*Table 15: List of G&D mainstreaming activities for year 1398*

S. No.	Activity	Deadline	Progress Tracking
1	Improve the annual plan of the IPs based on NMA SP Goals.	June 2019	

2	Advocate for independent budgeting for gender in proposals both with UNMAS and donors.	Through the year	
3	Conduct three events in relation with gender and awareness raising on mine action.	Through the year	
4	Follow up the new mechanism for the gender mainstreaming balance score card.	Through the year	
5	Review all DMAC QA forms as per gender mainstreaming requirement and facilitate the review of IP forms.	July 2019	
6	Conduct two gender awareness training in two regions (central and east regions).	December 2019	
7	Advocate for and support gender inclusion in IPs' organizational structures.	April 2019	
8	Advocate for and support gender capacity building for IP gender focal points.	Through the year	
9	Advocate for a gender officer to participate in QA of MRE and VA teams.	Through the year	
10	Advocate for gender officers to participate in survey and clearance teams.	each quarter	
11	Support the MAPA IPs in hiring dedicated G&D focal points.	As soon as possible	
12	Establish networks with organizations in the field of G&D and PwDs.	June 2019	
13	Awareness raising through different social events for Women's Day.	Every year 8 <sup>th</sup> March	
14	Implementation of gender markers (2a and 2b).	In every quarter	

## Chapter Three: Roles and Responsibilities

The MAPA consists of different stakeholders and the programme is present in most parts of the country. Mine and ERW contamination is scattered in all 34 provinces and much of the contamination is in communities where people have been displaced, refugees are returning, or where tensions between the government and AGE forces periodically erupt. The main stakeholders of the MAPA are the GoIRA, the implementing partners, donors, UNMAS, ITF Enhancing Human Security (ITF), Norwegian People’s Aid (NPA), UN agencies, the communities, and the development sector. They all have a role to play in the continued advancement of the MAPA vision. This table highlights the role and responsibilities expected of all stakeholders.

*Table 16: MAPA stakeholder's tasks and responsibilities in 1398*

Task	Details	Responsibility
Resource Mobilization	Meet with donors and advocate at public events to fund Mine Action	All stakeholders (DMAC, IPs, UNMAS, donors)
Communicate resource mobilization attempts related to specific hazard sites.	To assist in coordination and avoid inefficiency, report all donor engagement related to specific hazard sites to the DMAC in a timely manner.	UNMAS, donors and IPs
Quality Assurance and Control Inspection	<ul style="list-style-type: none"> <li>• IPs conduct internal QA/QC of their activities</li> <li>• DMAC to conduct QA/QC inspections monthly for each mine action project (bilaterally funded and VTF)</li> <li>• Conduct performance measurement through balanced scorecard</li> </ul>	DMAC/IPs
Escalation of QA/QC non-conformity reports.	Escalate details of non-conformities to relevant donors, along with any corrective actions undertaken or recommended.	DMAC
Grant/Contract compliance and oversight	Conduct project compliance and monitoring inspections to ensure projects are in line with intended results and improve future project design.	UNMAS for VTF; Norwegian People’s Aid (NPA) for PM/WRA
Project Management	Management of project activities efficiently from start to finish, including regular reporting.	IPs
Funding agreements and project document	Share project document (prior to submitting to donors) and funding agreement with DMAC for planning and coordination purposes.	Donors and IPs
Evaluation	Conduct post-demining impact assessments (PDIA) of 75 closed contaminated areas (10 per cent of all hazards closed in 1396). Conduct livelihood survey in 12 communities, 4 districts of Khost province.	DMAC
Reporting	Provision of mine action operational data, milestone reports and project closure reports.	DMAC, UNMAS and IPs

## Chapter Four: Risk Management

Table 17: List of Challenges and its mitigating measures

Challenges	Mitigating Measures
<b>Funding</b>	
The shortfall in funding poses a threat to the achievement of the targets set for 1398. Almost 27 per cent of the required funding has been secured as of March 2019.	To accelerate fund raising efforts, increase donor meetings, workshops, and advocacy; work with the government to facilitate new funding channels and opportunities.
<b>Security</b>	
The unstable security situation poses challenges and could disrupt operations.	The MAPA intends to enhance community liaison to educate communities on the importance and impartiality of the programme and conduct refresh visits to targeted areas to be cleared during the year to ensure validity and accessibility of the contaminated areas for further planning.
<b>Survey</b>	
<ul style="list-style-type: none"> <li>a) Security</li> <li>b) Increased number of actual villages compared to the gazetteer</li> <li>c) Funding</li> </ul>	<ul style="list-style-type: none"> <li>a) Maintaining strong community liaison and close contact with influential people and community elders, community shuras, etc. in relevant locations will help with security restrictions for the survey teams.</li> <li>b) Make an estimation of actual villages not in the gazetteer based on previous experience of surveys completed in other districts.</li> <li>c) Increase efforts on fundraising.</li> </ul>
<b>Clearance</b>	
<ul style="list-style-type: none"> <li>a) Accessibility</li> <li>b) Change of project area due to security constraints</li> </ul>	Demining teams as well as DMAC ROs, ACBL and UNMAS CTG access employees should keep and maintain close liaison with community elders and influential people of the communities in order to facilitate mine action intervention and provide a response to the most at-risk people.
<b>Mine/ERW Risk Education</b>	
Physical access to implement Mine/ ERW Risk Education is challenging in conflict affected/ disputed areas.	IPs to recruit and deploy Risk Education trainers from the local communities, who can speak the

	<p>language and are familiar with local customs and traditions.</p> <p>Train and deploy volunteers from local communities.</p> <p>Use most relevant media as an alternative (indirect) approach to disseminate Mine/ ERW Risk Education messages in insecure areas.</p> <p>IPs to have a clear security policy and plan.</p>
<b>Victim Assistance</b>	
<p>Physical Rehabilitation: the number of rehabilitation centres and qualified staff is low, and access to these centres is impacted by distance and conflict.</p>	<p>Support MoPH by training physiotherapists and prosthetic/orthotic technicians (direct training or on the job training by IPs) including female technicians.</p> <p>Mobile clinics assist in mitigating access constraints.</p>
<p>Social Inclusion and Advocacy: negative stereotypes of girls and other marginalized groups such as child survivors &amp; and other children with disabilities further limits access to education.</p> <p>Women with disabilities, including female survivors, are often excluded from certain social roles, such as marriage and parenting.</p>	<p>Victim assistance interventions should include an element of inclusivity and rights awareness to sensitise persons with disabilities to their rights and the communities to reducing barriers to their inclusion.</p> <p>The community-based rehabilitation guides, National Disability plan, Inclusive Education guide books and sign language books should be printed and translated widely to increase disability awareness and provide support to vulnerable people in social inclusion.</p>
<p>Data collection: shortage of a comprehensive database with up to date data that gives an accurate picture of the number and scope of the problem of people with disability</p>	<p>Support MMD and The Asia Foundation in conducting a nationwide disability survey and advocate for a meaningful utilisation of the MMD database; which is being developed.</p> <p>The Conflict Mitigation Assistance for Civilians (COMAC) surveyors will collect data, including data on people with disabilities.</p> <p>1,000 community health workers will support the data collection process.</p> <p>Support MMD in creation of a central database for disability.</p>

## Annex A. 1398 Demining Projects, targeted and planned as of July 2019

Project Name	Province	Project fund Status	Start Date	End Date	Area of Confirm Fund	Area of Pledged fund	Area of unfound	Channel	Donor	Agency
Baghlan Demining Project-22/C	Baghlan	Confirm	1/Jan/18	10/Jan/19	679,942			VTF	UNMAS	ATC
DDG Parwan and Bamyan VTF Demining Project-1398	Bamyan, Parwan	Confirm	3/Apr/19	3/Dec/19	711,251			VTF	UNMAS	DDG
HT VTF Baghlan Demining Project-1398	Baghlan	Confirm	19/Feb/19	31/Jan/20	1,227,400			VTF	UNMAS	HT
AFG/UNMAS/21215/2018/010	Farah	Confirm	10/Oct/18	30/Nov/19	1,433,741			VTF	UNMAS	ATC
AFG/UNMAS/21215/2018/012	Kandahar	Confirm	2/Oct/18	31/Jul/19	3,245,377			VTF	UNMAS	DAFA
ATC Takhar and Baghlan VTF Demining Project-1398	Baghlan, Takhar	Confirm	15/Mar/19	15/Dec/19	1,497,093			VTF	UNMAS	ATC
DAFA VTF Hirat Demining Project-1398	Hirat	Confirm	1/Jan/18	31/Mar/20	3,450,533			VTF	UNMAS	DAFA
HT VTF Maydan Wardak Demining Project-1398	Maydan Wardak	Confirm	1/Mar/19	31/Dec/19	1,094,503			VTF	UNMAS	HT
MCPA/DAFA VTF Nimroz Demining Project-1398	Nimroz	Confirm	15/Jun/19	31/Mar/20	2,052,052			VTF	UNMAS	MCPA
OMAR VTF Logar Demining Project-1398	Logar	Confirm	05-May-19	13-Feb-20	4,132,779			VTF	UNMAS	OMAR
Provision of Regional Mine Action Quick Response Capacity in Afghanistan	Balkh, Ghazni, Hilmand, Paktika	Confirm	1/Jan/19	28/Feb/20	1,601,184			VTF	UNMAS	HT
MCPA/DAFA VTF Demining Project-2019	Zabul	Confirm	4/Jun/19	31/Dec/19	6,517,895			VTF	UNMAS	MCPA
DDG DANIDA Demining Project-2019	Kabul	Confirm	1/Jan/19	31/Dec/19	330,956			Bilateral	DANIDA	DDG
HT Finland Demining Project-1398	Baghlan, Parwan, Samangan, Takhar	Confirm	1/Jan/19	31/Dec/19	2,333,524			Bilateral	Finland	HT
Hilmand AIM Clearance Project-01	Hilmand	Confirm	1/Jan/19	30/Jun/19	841,364			Bilateral	Germany	HT
HT GFFO MC Demining Project 2019-2020	Baghlan, Balkh,	Confirm	1/Jan/19	30/Jun/19	2,799,873			Bilateral	Germany	HT



Project Name	Province	Project fund Status	Start Date	End Date	Area of Confirm Fund	Area of Pledged fund	Area of unfound	Channel	Donor	Agency
	Parwan, Samangan									
Kandahar Demining Project-04 AT/E	Kandahar	Confirm	1/Jan/19	31/Dec/19	1,351,607			Bilateral	Ireland	HT
AREA GAGP Demining Project-1398	Nangarhar	Confirm	1/Mar/19	31/Jan/20	323,606			Bilateral	Japan	AREA
HT AAR Demining Project 1398	Baghlan	Confirm	1/Jun/19	30/Dec/19	39,394			Bilateral	Japan	HT
OMAR GAGP Demining Project-1398	Kapisa, Parwan	Confirm	27/Feb/19	26/Feb/20	594,442			Bilateral	Japan	OMAR
HT AIM Survey + Clearance project 1397/1398	Hilmand	Confirm			19,357			Bilateral	Netherlands	HT
HT RNG Demining Project 2019	Baghlan, Kabul, Samangan	Confirm	1/Jan/19	31/Dec/19	1,379,261			Bilateral	Netherlands	HT
Kandahar Demining Project-01/H	Kandahar	Confirm	1/Jul/19	30/Jun/20	1,375,052			Bilateral	Norway	HT
FSD PATRIP Demining Project-2019	Badakhshan	Confirm	1/Jan/19	31/Dec/19	151,594			Bilateral	PATRIP	FSD
DDG SIDA Demining Project-2019	Balkh, Samangan	Confirm	1/Jan/18	31/Dec/21	422,031			Bilateral	SIDA	DDG
HT CSSF Demining Project-1398	Baghlan, Balkh, Logar, Samangan	Confirm	1/Apr/19	31/Mar/20	6,284,727			Bilateral	UK-CSSF	HT
Badakhshan Demining Project-03/D	Badakhshan	Confirm	1/Jan/18	31/Dec/19	313,704			Bilateral	USDoS	FSD
Baghlan Demining Project-03/F	Baghlan	Confirm	1/Jul/18	30/Jun/19	146,781			Bilateral	USDoS	DDG
Nangarhar Demining Project-06	Nangarhar	Confirm	1/Jul/18	30/Jun/19	106,054			Bilateral	USDoS	DDG
NOFO Project-16 Panjshir	Panjsher	Confirm	1/Jul/18	30/Jun/19	242,453			Bilateral	USDoS	DDG
Panjshir Demining Project-05/B	Panjsher	Confirm	1/Jul/18	30/Jun/19	389,062			Bilateral	USDoS	DDG
Parwan Demining Project-14	Parwan	Confirm	1/Jul/18	30/Jun/19	126,053			Bilateral	USDoS	DDG
HT/DACAAR VTF Kandahar Demining Project-1398	Kandahar	Confirm	1/Jul/19	31/Mar/20	1,561,424			Bilateral	USDoS	HT
Kabul Demining Project-19/C	Kabul	Confirm	1/Apr/18	31/Jul/19	1,280			Bilateral	USDoS	HT
Kapisa Demining Project-02	Kapisa	Confirm	1/Apr/18	31/Jul/19	356,237			Bilateral	USDoS	HT
Logar Demining Project-01 (AT)	Logar	Confirm	1/Apr/18	31/Jul/19	191,378			Bilateral	USDoS	HT
Maydan Wardak Demining Project-05/B	Maydan Wardak	Confirm	25/Sep/17	24/Sep/19	182,796			Bilateral	USDoS	DAFA

Project Name	Province	Project fund Status	Start Date	End Date	Area of Confirm Fund	Area of Pledged fund	Area of unfound	Channel	Donor	Agency
Nangarhar Demining Project-05/G	Nangarhar	Confirm	25/Sep/17	24/Sep/19	635,900			Bilateral	USDoS	DAFA
NOFO Project 26 Panjsher-Nangarhar	Nangarhar, Panjsher	Confirm	1/Jul/19	30/Jun/20	1,322,426			Bilateral	USDoS	HT
NOFO Project-20 Baghlan and Laghman	Baghlan, Laghman	Confirm	1/May/19	30/Apr/20	3,527,912			Bilateral	USDoS	HT
NOFO Project-21 Baghlan and Kunar	Baghlan, Kunar	Confirm	17/Jun/19	30/Apr/20	6,127,902			Bilateral	USDoS	ATC
NOFO Project-22 Kandahar	Kandahar	Confirm	20/Jun/19	19/Jun/20	5,627,206			Bilateral	USDoS	ATC
NOFO Project-23 Samangan-Balkh-Khost	Balkh, Khost, Samangan	Confirm	1/Jul/19	30/Jun/20	3,039,519			Bilateral	USDoS	HT
NOFO Project-24 Maydan Wardak-Nimruz	Maydan Wardak, Nimroz	Confirm	1/Jun/19	31/May/20	3,340,642			Bilateral	USDoS	DAFA
NOFO Project-25 Kapisa-Baghlan-Khost	Baghlan, Kapisa, Khost	Confirm	1/May/19	30/Apr/20	1,383,563			Bilateral	USDoS	DAFA
Parwan Demining Project-08/A	Parwan	Confirm	1/Apr/18	31/Jul/19	219,212			Bilateral	USDoS	HT
Takhar Demining Project-03/A	Takhar	Confirm	25/Sep/17	24/Sep/19	963,424			Bilateral	USDoS	DAFA
Baghlan Demining Project-06	Baghlan	Pledged				693,042		VTF	UNMAS	
Kunar Demining Project-03	Kunar	Pledged				3,633,469		VTF	UNMAS	
Nangarhar Demining Project-03/I	Nangarhar	Pledged				713,500		VTF	UNMAS	
Nangarhar Demining Project-03/J	Nangarhar	Pledged				3,247,043		VTF	UNMAS	
Paktya Demining Project-03/C	Paktya	Pledged				341,568		VTF	UNMAS	
Paktya Demining Project-03/E	Paktya	Pledged				575,501		VTF	UNMAS	
Paktya Demining Project-06	Paktya	Pledged				786,605		VTF	UNMAS	
Hirat Demining Project-03	Hirat	Pledged				1,410,437		Bilateral	DOS	ATC
Hirat Demining Project-04	Hirat	Pledged				2,669,460		Bilateral	DOS	ATC
Kabul Demining Project-19/G	Kabul	Pledged				414,966		Bilateral	DOS	AREA
Kunduz Demining Project-04	Kunduz	Pledged				860,781		Bilateral	DOS	OMAR
Kunduz Demining Project-04/A	Kunduz	Pledged				149,911		Bilateral	DOS	OMAR
Logar Demining Project-01 (AT)/E	Logar	Pledged				1,353,000		Bilateral	DOS	HT
Nangarhar Demining Project-03/H	Nangarhar	Pledged				194,157		Bilateral	DOS	MDC
Nangarhar Demining Project-05/B	Nangarhar	Pledged				195,989		Bilateral	DOS	MDC

Project Name	Province	Project fund Status	Start Date	End Date	Area of Confirm Fund	Area of Pledged fund	Area of unfound	Channel	Donor	Agency
Panjshir Demining Project-05/A	Panjshir	Pledged				126,956		Bilateral	DOS	AREA
Panjshir Demining Project-05/G	Panjshir	Pledged				449,000		Bilateral	DOS	AREA
Takhar Demining Project-08/C	Takhar	Pledged				934,098		Bilateral	DOS	MDC
Maydan Wardak Demining Project-10/A	Maydan Wardak	Unfunded					846,322			
Faryab AIM Clearance Project-01	Faryab	Unfunded					957,804			
Khost Demining Project-05/A	Khost	Unfunded					22,699			
Hilmand Demining Project-02 AT/B	Hilmand	Unfunded					435,007			
Hilmand AIM Clearance Project-02	Hilmand	Unfunded					1,735,379			
Hilmand AIM Clearance Project-05	Hilmand	Unfunded					4,053,985			
Hilmand AIM Clearance Project-06	Hilmand	Unfunded					419,798			
Takhar Demining Project-08/I	Takhar	Unfunded					104,962			
Balkh Demining Project-1/Q	Balkh	Unfunded					1,765,298			
Parwan Demining Project-08	Parwan	Unfunded					264,799			
Badakhshan Demining Project-05	Badakhshan	Unfunded					196,345			
Maydan Wardak Demining Project-03 (AT)/A	Maydan Wardak	Unfunded					6,190,458			
Kunduz Demining Project-03/B	Kunduz	Unfunded					2,787,969			
Kandahar Demining Project-04 AT/B	Kandahar	Unfunded					608,920			
Nangarhar Demining Project-04	Nangarhar	Unfunded					831,065			
Paktya Demining Project-03 AT/A	Paktya	Unfunded					65,000			
Maydan Wardak Demining Project-07 (AT)	Maydan Wardak	Unfunded					950,355			
Parwan Demining Project-15	Parwan	Unfunded					41,610			
Logar Demining Project-03 (AT)	Logar	Unfunded					1,017,013			
Ghazni Demining Project-01/A	Ghazni	Unfunded					7,623,753			
Hilmand AIM Clearance Project-03	Hilmand	Unfunded					1,306,168			
Ghazni Demining Project-02/B	Ghazni	Unfunded					506,484			
Hilmand AIM Clearance Project-04	Hilmand	Unfunded					234,625			
Logar Demining Project-03/D	Logar	Unfunded					1,448,178			
Jawzjan Demining Project-1/B	Jawzjan	Unfunded					133,215			
Baghlan Demining Project-04	Baghlan	Unfunded					530,865			

Project Name	Province	Project fund Status	Start Date	End Date	Area of Confirm Fund	Area of Pledged fund	Area of unfound	Channel	Donor	Agency
Kandahar Demining Project-01/G	Kandahar	Unfunded					7,494,612			
Kunar Demining Project-02/D	Kunar	Unfunded					1,570,550			
Kandahar Demining Project-04 AT/F	Kandahar	Unfunded					3,842,450			
Nangarhar Demining Project-03/G	Nangarhar	Unfunded					895,183			
Kabul Demining Project-19/F	Kabul	Unfunded					51,698			
<b>Total</b>					75,695,464	18,749,483	48,932,569			

## Annex B. List of NTS Planned Districts for 1398

S/No	Region	Province	District	Remarks
1	Center	Bamyan	Kahmard	Funded by PM/WRA
2	Center	Parwan	Sia Gird	Funded by PM/WRA
3	Center	Parwan	Shinwari	Funded by PM/WRA
4	Center	Maydan Wardak	Jalriz	Funded by PM/WRA
5	East	Nangarhar	Goshta	Funded by UNMAS
6	East	Nangarhar	Lal Pur	Funded by PM/WRA
7	East	Nangarhar	Kot	Funded by PM/WRA
8	East	Laghman	Alishang	Funded by PM/WRA
9	East	Laghman	Dawlat Shahi	Funded by PM/WRA
10	East	Laghman	Alingar	Funded by UNMAS
11	North	Balkh	Balkh	Funded by UNMAS
12	North	Sari Pul	Sari Pul	Funded by UNMAS
13	North East	Kunduz	Imam Sahib	Funded by PM/WRA
14	North East	Kunduz	Ali Abad	Funded by PM/WRA
15	North East	Baghlan	Dushi	Funded by PM/WRA
16	South	Hilmand	Nad Ali	Funded by PM/WRA
17	South	Hilmand	Nahri Sarraj	Funded by UNMAS
18	South	Kandahar	Ghorak	Funded by PM/WRA
19	South	Kandahar	Maruf	Funded by PM/WRA
20	South	Kandahar	Miya Nishin	Funded by PM/WRA
21	South	Zabul	Tarnak wa Jaldak	Funded by PM/WRA
22	South	Zabul	Shinkay	Funded by PM/WRA
23	South East	Paktya	Ahmad Abad	Funded by UNMAS
24	South East	Paktya	Lija Ahmad Khel	Funded by UNMAS
25	South East	Paktya	Ali Khel	Funded by UNMAS
26	South East	Paktya	Dand wa Patan	Funded by PM/WRA
27	South East	Paktya	Shwak	Funded by PM/WRA
28	South East	Khost	Spira	Funded by PM/WRA
29	South East	Khost	Qalandar	Funded by UNMAS
30	West	Farah	Balabuluk	Funded by UNMAS



THE DIRECTORATE OF MINE  
ACTION COORDINATION (DMAC)

SEDARAT SQUARE,  
KABUL, AFGHANISTAN  
+93(0) 708 60 60 60  
INFO@DMAC.GOV.AF  
WWW.DMAC.GOV.AF

DEVELOPED BY THE DIRECTORATE OF MINE ACTION COORDINATION (DMAC)  
MARCH 2019
